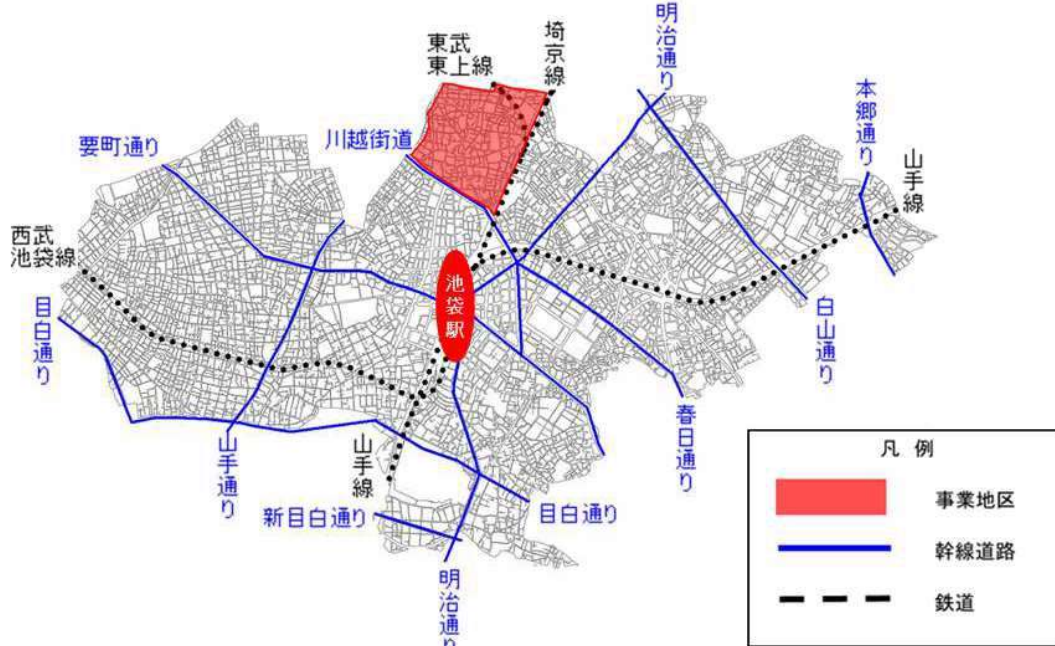
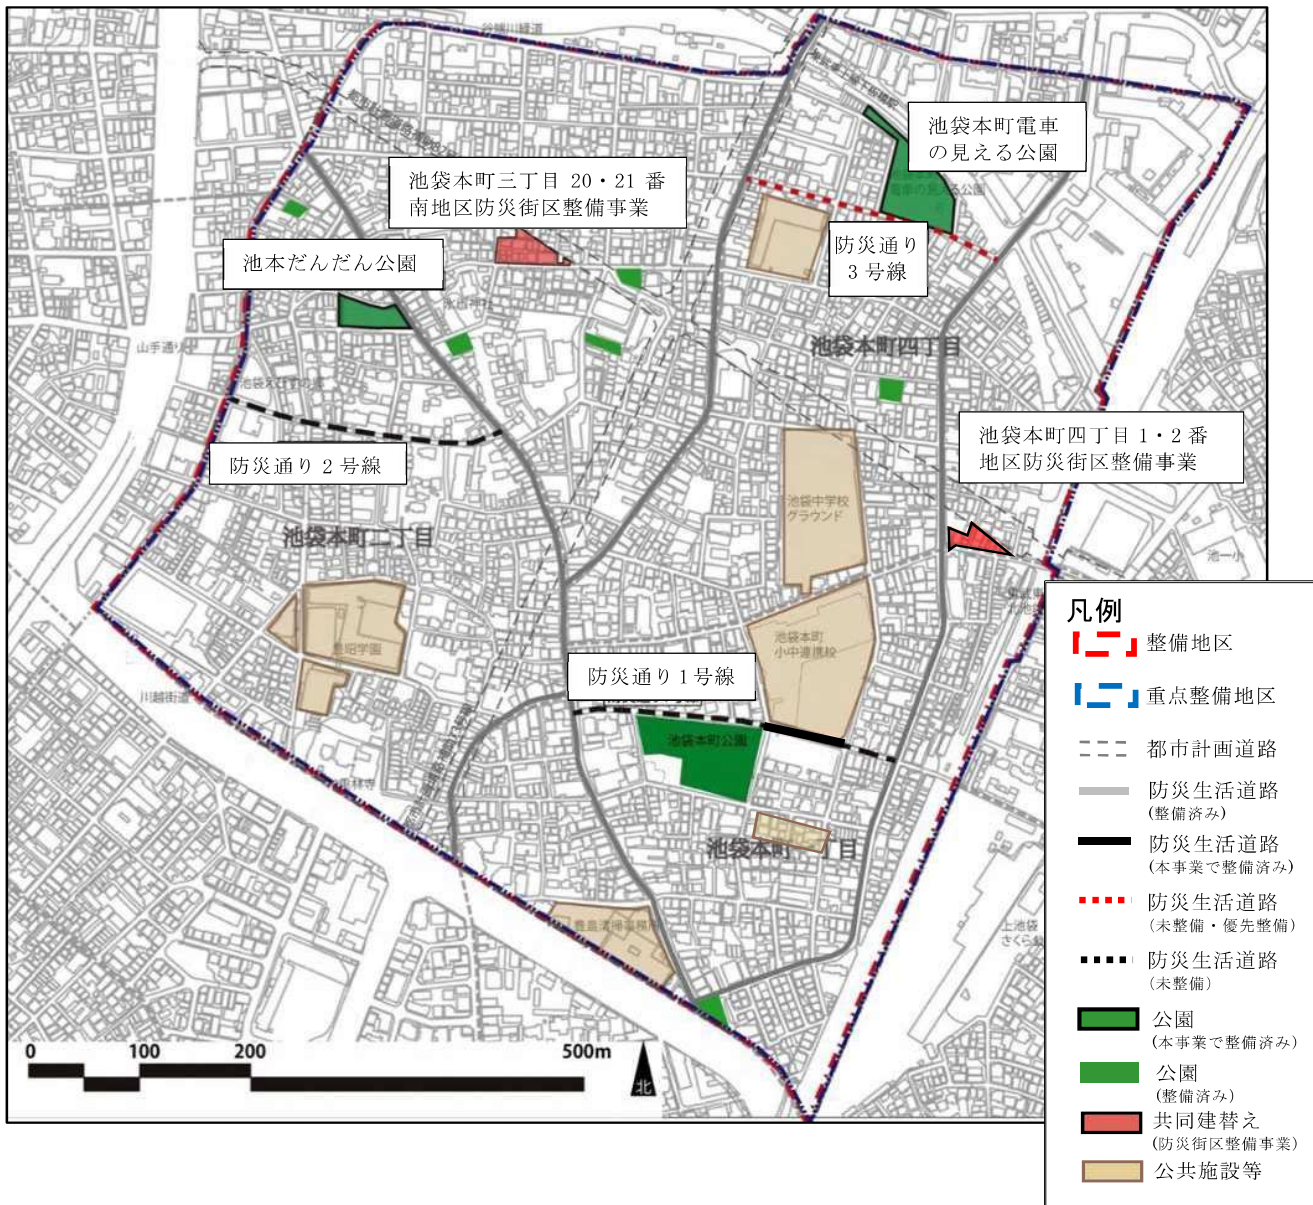


評価対象事業案内（１）			番号	令和６年度２号																																													
位置図 			事業内容を示す図面 																																														
事業概要 <table><tr><th colspan="2" rowspan="2">対象項目</th><th colspan="3">現行計画（見直し前）</th><th colspan="2">見直し案</th></tr><tr><th>整備計画内容（A）</th><th>実績 令和6年度末時点（B）</th><th>進捗率（B／A）</th><th>整備計画内容（A'）</th><th>増減（A'－A）</th></tr><tr><td rowspan="2">道路</td><td>取得</td><td>926.00㎡</td><td>668.00㎡</td><td>72%</td><td>817.44㎡</td><td>▲108.56㎡</td></tr><tr><td>整備</td><td>1,703.00㎡</td><td>202.50㎡</td><td>12%</td><td>1,702.50㎡</td><td>▲0.50㎡</td></tr><tr><td>細街路</td><td>整備</td><td>2,146.00㎡</td><td>1,662.90㎡</td><td>77%</td><td>2,146.00㎡</td><td>±0㎡</td></tr><tr><td rowspan="2">公園 緑地 広場</td><td>取得</td><td>6,920.00㎡</td><td>5,680.57㎡</td><td>82%</td><td>7,180.57㎡</td><td>+260.57㎡</td></tr><tr><td>整備</td><td>6,720.00㎡</td><td>5,480.50㎡</td><td>82%</td><td>6,980.50㎡</td><td>+260.50㎡</td></tr></table>			対象項目		現行計画（見直し前）			見直し案		整備計画内容（A）	実績 令和6年度末時点（B）	進捗率（B／A）	整備計画内容（A'）	増減（A'－A）	道路	取得	926.00㎡	668.00㎡	72%	817.44㎡	▲108.56㎡	整備	1,703.00㎡	202.50㎡	12%	1,702.50㎡	▲0.50㎡	細街路	整備	2,146.00㎡	1,662.90㎡	77%	2,146.00㎡	±0㎡	公園 緑地 広場	取得	6,920.00㎡	5,680.57㎡	82%	7,180.57㎡	+260.57㎡	整備	6,720.00㎡	5,480.50㎡	82%	6,980.50㎡	+260.50㎡	見直し概要 - 事業延伸に伴う整備内容の見直しはせず、令和２年度から令和６年度で実施できなかった残事業に取り組んでいく。 - 今後６年間において、防災生活道路（計画路線）３路線の内、防災通り３号線を優先して、用地買収を主とした公共整備型の事業を進め、令和１２年度の完了を目指す。 - 公園３箇所の整備を目指す。 - 都市計画道路沿道において防災街区整備事業による老朽住宅等の建替えを促進する。すでに準備組合が令和４年度に設立されており、完了予定は令和１０年度内を目指している。	
対象項目		現行計画（見直し前）			見直し案																																												
		整備計画内容（A）	実績 令和6年度末時点（B）	進捗率（B／A）	整備計画内容（A'）	増減（A'－A）																																											
道路	取得	926.00㎡	668.00㎡	72%	817.44㎡	▲108.56㎡																																											
	整備	1,703.00㎡	202.50㎡	12%	1,702.50㎡	▲0.50㎡																																											
細街路	整備	2,146.00㎡	1,662.90㎡	77%	2,146.00㎡	±0㎡																																											
公園 緑地 広場	取得	6,920.00㎡	5,680.57㎡	82%	7,180.57㎡	+260.57㎡																																											
	整備	6,720.00㎡	5,480.50㎡	82%	6,980.50㎡	+260.50㎡																																											
事業の種類		密集市街地総合防災事業																																															
事業の名称		池袋本町地区																																															
評価の実施主体		豊島区																																															
事業所管部署		豊島区 都市整備部 地域まちづくり課																																															
評価該当要件		５年間未着工・10年間継続・その他（ ）																																															
対応方針（案）		継続・中止																																															

番号 令和6年度2号

This map illustrates the disaster prevention areas and facilities in Ikusagaya Town. The town is divided into several blocks (chome), with specific areas highlighted for disaster prevention work. Key features include:

- Disaster Prevention Areas:** Indicated by red dashed lines and labels such as "池袋本町三丁目 20・21 番南地区防災街区整備事業" (Ikusagaya Honcho 3-chome 20・21-ban South Area Disaster Prevention Area Improvement Project) and "池袋本町四丁目 1・2 番地区防災街区整備事業" (Ikusagaya Honcho 4-chome 1・2-ban Area Disaster Prevention Area Improvement Project).
- Disaster Prevention Routes:** Labeled as "防災通り 1号線" (Disaster Prevention Route 1), "防災通り 2号線" (Disaster Prevention Route 2), and "防災通り 3号線" (Disaster Prevention Route 3).
- Facilities and Landmarks:**
 - Parks:** 池本だんだん公園 (Ikumoto Dandan Park), 池袋本町公園 (Ikusagaya Honcho Park), and 池袋本町電車の見える公園 (Ikusagaya Honcho Electric Train Visible Park).
 - Schools:** 池袋中学校 (Ikusagaya Junior High School), 池袋本町小学校 (Ikusagaya Honcho Elementary School), and 池袋本町幼稚園 (Ikusagaya Honcho Kindergarten).
 - Other Landmarks:** 池袋本町グラウンド (Ikusagaya Honcho Ground), 池袋本町郵便局 (Ikusagaya Honcho Post Office), and 池袋本町駅前 (Ikusagaya Honcho Station Front).
- Photograph Locations:** Six specific locations are marked with black boxes and labeled "写真①" through "写真⑥" (Photo 1 through Photo 6), indicating where photographs were taken during the survey.
- Scale and Orientation:** A scale bar at the bottom left shows distances from 0 to 500 meters. A north arrow is located at the bottom center.

事業の種類	密集市街地総合防災事業
事業の名称	池袋本町地区
評価の実施主体	豊島区
事業所管部署	豊島区 都市整備部 地域まちづくり課
評価該当要件	5年間未着工・ <u>10年間継続</u> ・その他（ ）
	<u>継続</u> ・中止

